ROADSENSE | Infrastructure Intelligence

DATE: November 08, 2026
STANDARD: ASTM D6433 / IRI

ASTM D6433 CONDITION	ROUGHNESS INDEX (IRI)	MATERIAL REQUIRED	ESTIMATED REPAIR BUDGET
10.0 / 100 **Serious / Failed**	**4.32** m/km ASTM E1926	**22.6 kg** Cold-Mix Bitumen	**Rs. 3267** ($108.24)

Hazard Classification & Severity Breakdown

Hazard Category	Impact Severity	Count	Recommended Municipal Action
Pothole	Severe (Z >= 3.0)	1	Immediate Cold Patching / Asphalt Mill & Infill (<48h)
Pothole	Moderate (Z 2.0-3.0)	1	Scheduled Maintenance (<14 days)
Pothole	Minor / Anomaly (Z < 2.0)	5	Surface Seal Coating / Monitor
Speedbreaker	Standard Deflection	1	Verify Regulatory Height & Signage Painting

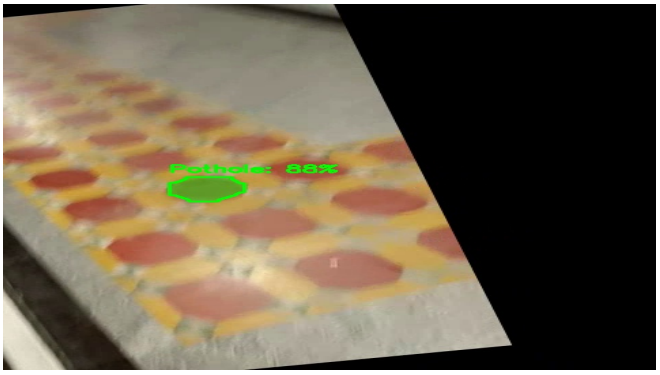
Priority Maintenance Dispatch Table (Top Critical Hazards)

ID	Type	Severity	Latitude	Longitude	Dimensions	Bitumen Mass	Est. Budget	Action
#01	Speedbreaker	Severe	12.922398	77.501601	958cm² x 8.8cm	9.9 kg	Rs.745	Emergency Patch
#02	Pothole	Moderate	12.922396	77.501614	1819cm² x 4.9cm	10.5 kg	Rs.772	Routine Repair
#03	Pothole	Low	0.000000	0.000000	150cm² x 2.5cm	0.5 kg	Rs.350	Routine Repair
#04	Pothole	Low	12.922398	77.501601	150cm² x 2.5cm	0.5 kg	Rs.350	Routine Repair
#05	Pothole	Low	12.922398	77.501601	150cm² x 2.5cm	0.5 kg	Rs.350	Routine Repair
#06	Pothole	Low	12.922398	77.501601	150cm² x 2.5cm	0.5 kg	Rs.350	Routine Repair
#07	Pothole	Low	0.000000	0.000000	150cm² x 2.5cm	0.5 kg	Rs.350	Routine Repair

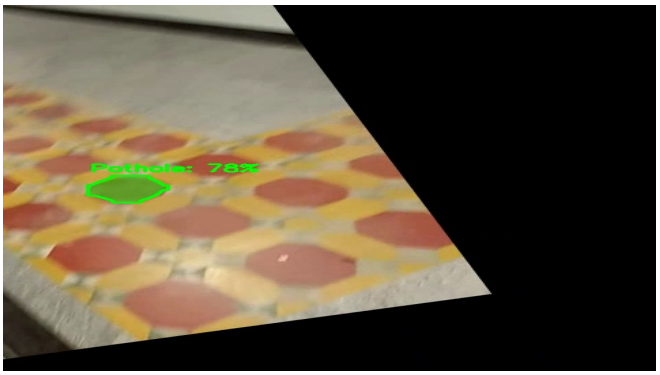
Camera Ground-Truth Evidence (AI Detection Bounding Boxes)

Visual verification frames captured by vehicle optical sensors at timestamp of impact.


Pothole: 62%


Pothole: 88%


Pothole: 80%


Pothole: 78%
